GCP Migration Program: Monthly Stakeholder Report

Month 4 · end of week 17

For the executive sponsor and steering committee. Figures are illustrative.

Prepared by Balakrishna Pallapolu, program lead

Month 4 is amber; the end date holds

AMBER

9 of 20 applications live against a plan of 10

Wave 1 moved 7 of its 8 applications on schedule with no rollbacks. One Tier 1 application, A-07, failed its cutover rehearsal: the final database sync took 5 hours 40 minutes against a 4-hour window. It is rescheduled to week 18. Wave 2 is on plan and the week 26 end date holds.

Decision needed

Approve one six-hour weekend window for A-07 in week 18. The alternative is a phased database migration that adds two weeks and uses all remaining contingency.

9 of 20

applications live; plan was 10

9 of 9

first-time cutovers, no rollbacks

0

open Severity 1 or 2 incidents

61%

of budget spent; plan was 59%

Achieved this month


- Seven Platform A applications cut over, two of them Tier 1
- One Severity 2 incident in hypercare, closed in three days
- Average cutover time down from 3h 10m to 2h 20m

One application is two weeks behind plan

Milestone	Planned	Forecast	Status	Comment
M1 Mobilize and discover	Week 4	Done week 4	Complete	Baseline approved
M2 Foundations ready	Week 8	Done week 8	Complete	Security sign-off received
M3 Pilot	Week 10	Done week 10	Complete	Re-forecast confirmed the plan
M4 Wave 1: Platform A	Week 16	Week 18	Amber	7 of 8 live; A-07 outstanding
M5 Wave 2: Platform B	Week 22	Week 22	Green	6 of 10 builds complete; cutovers start week 18
M6 Resilience proven	Week 24	Week 24	Not started	Exercise scenario in draft
M7 Stabilize and hand over	Week 26	Week 26	Not started	Starts week 24

Green: on plan. Amber: a gate is at risk and has a recovery path. Red: a gate will be missed without a steering decision.

Migration is one application short of plan

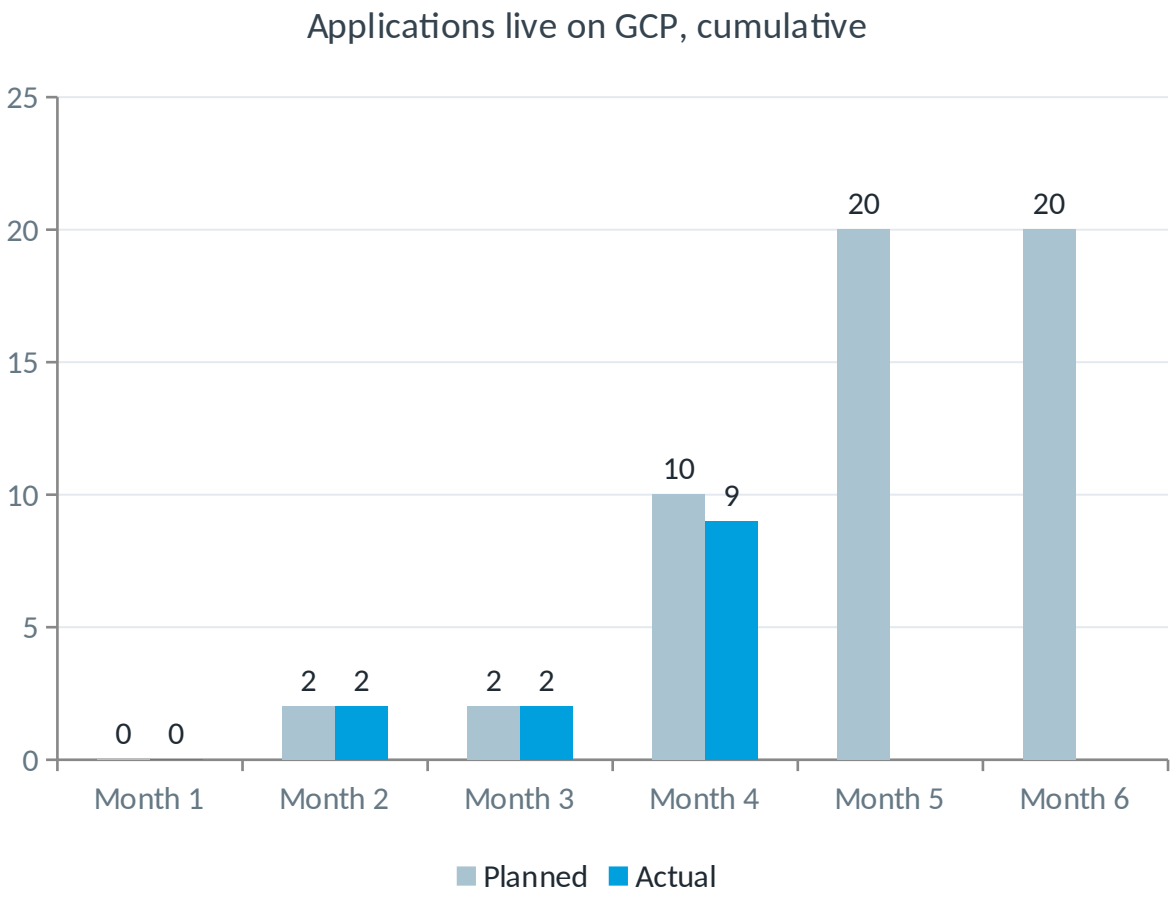

Measure	This month	Target
First-time cutover success	9 of 9	At least 90%
Rehearsals inside the window	9 of 10	All before go
Zone failover tests passed	9 of 9	All live
Peak Tier 1 replica lag	40 seconds	Under 5 minutes
Open Severity 1 and 2	0	0
Spend to date	61%	59% planned
Contingency used	0 of 2 weeks	Steering approval

Remaining migration contingency is now earmarked for A-07.

Three risks and issues need attention

Item	Type	Status	Action	Owner
A-07 cutover exceeds its 4-hour window	Issue	Amber	Replication re-tuned; second rehearsal in week 17 ran 5 hours 10 minutes; six-hour window requested	Database lead
Platform B team at 22 percent capacity against 30 percent agreed	Risk	Amber	Raised with sponsor; two features proposed for deferral	Executive sponsor
Business owners not yet confirmed for the DR exercise in week 23	Risk	Green	Invitations issued; confirmation due week 19	SRE lead

Two decisions, then the final wave

Decisions needed

1. Approve a six-hour weekend window for A-07 in week 18.
The alternative is a phased database migration, which adds two weeks and uses all remaining contingency.

2. Confirm Platform B team capacity at 30 percent through week 21.
Without it, Tier 1 cutovers in weeks 20 to 21 are at risk.

Next month

- Cut over A-07 and all 10 Platform B applications, weeks 18 to 21
- Approve the DR exercise plan and start load testing
- Reach gate G5: all 20 applications live by week 22
